



City of Killeen
Engineering Division

Project Status Report
FY26 Quarter 1
January 2026

SECTION I ACTIVE DESIGN AND PLANNING PROJECTS

1. **PROJECT NAME:** WILLOW SPRINGS RECONSTRUCTION

Project Manager: *Donald Wetzel*
Eng. Consultant: *K. Friese + Associates*
Contract % Complete: *48%*
Eng. Contract Amount: *\$877,798.81*
Amount Paid to Date: *\$420,421.69*
Preliminary Plan (30%) Due Date: *TBD*
Final Plan Due Date: *TBD*
Bid Set Due Date: *TBD*
Construction Estimate: *TBD*

TRANSPORTATION



COMMENTS: The project is on hold while Watercrest is under construction. The design will restart in 2026. The project will proceed to construction when funding is available.

2. **PROJECT NAME:** CHAPARRAL ROAD WIDENING

Project Manager: *Donald Wetzel*
Eng. Consultant: *Freese & Nichols, Inc.*
Contract % Complete: *24%*
Eng. Contract Amount: *\$7,880,570*
Amount Paid to Date: *\$1,908,812*
Preliminary Design (30%) Phase 1 Due Date: *Completed*
Final Phase 1 Plan Due Date: *March 2028*
Phase 1 Bid Set Due Date: *TBD*
Construction Estimate: *\$115,367,775*

TRANSPORTATION




COMMENTS: Project was resubmitted to TxDOT for environmental review due to a design change. The consultant is working on the final plans and collecting additional data through on-site surveying. The consultant has conducted on-site geo-technical borings, is coordinating with franchise utility owners, collected on-site traffic counts, and is reviewing drainage options.

3. PROJECT NAME: RANCIER IMPROVEMENTS

Project Manager: *Christopher Hoch*
Eng. Consultant: *BGE Inc.*
Contract % Complete: *21%*
Eng. Contract Amount: *\$10,282,040.05*
Amount Paid to Date: *\$2,167,437.26*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *October 2027*
Bid Set Due Date: *December 2027*
Construction Estimate: *\$61,755,000*

TRANSPORTATION

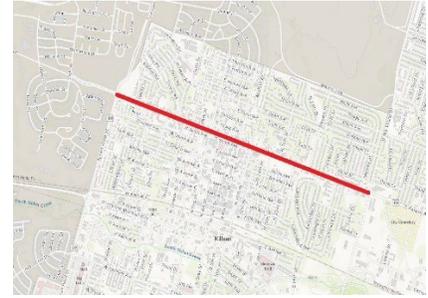

COMMENTS: The consultant has completed the 30% plans, which include landscape, lighting, and utility design. City staff have met with the consultant to discuss the 30% comments and review the landscaping improvements. The plans have been reviewed and returned to the consultant with comments for them to address.

4. PROJECT NAME: STAGECOACH RECONSTRUCTION PHASE 2

Project Manager: *Christopher Hoch*
Eng. Consultant: *Pape Dawson Engineers*
Contract % Complete: *25%*
Eng. Contract Amount: *\$230,000*
Amount Paid to Date: *\$58,500*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *Completed*
Bid Set Due Date: *January 2026*
Construction Estimate: *\$8,635,985*

TRANSPORTATION



COMMENTS: The consultant is preparing the Phase 2 bid documents, which are scheduled for completion by the end of January 2026. Bidding of this phase will occur once the current phase under construction nears completion. Phase 2 will extend from W.S. Young Drive to Highway 195.

- 5. PROJECT NAME: FEATHERLINE ROAD**
Project Manager: *Yul Eroy*
Eng. Consultant: *Kimley-Horn*
Contract % Complete: *28%*
Eng. Contract Amount: *\$2,017,641.26*
Amount Paid to Date: *\$556,635.77*
Preliminary Plan (30%) Due Date: *June 2025*
Final Plan Due Date: *July 2026*
Bid Set Due Date: *August 2026*
Construction Estimate: *TBD*

TRANSPORTATION



COMMENTS: Engineers are assessing whether a roundabout or a signalized intersection is the most practical and cost-effective option for the intersection of Malmaison St. The remaining design is progressing towards 30%.

- 6. PROJECT NAME: MOHAWK DRIVE**
Project Manager: *Christopher Hoch*
Eng. Consultant: *Pape Dawson*
Contract % Complete: *0%*
Eng. Contract Amount: *\$1,417,641.58*
Amount Paid to Date: *\$0*
Preliminary Plan (30%) Due Date: *February 2026*
Final Plan Due Date: *September 2026*
Bid Set Due Date: *October 2026*
Construction Estimate: *TBD*

TRANSPORTATION



COMMENTS: The design contract was approved by the City Council on October 21, 2025. The consultant has completed the survey work and has begun working on the roadway design, drainage design, and pedestrian facilities for the section of Mohawk Dr between Bunny Trail and Castle Gap Dr.

7. PROJECT NAME: HIGHWAY 195 ELEVATED STORAGE TANK WATER AND SEWER

Project Manager: *Steve Kana*
Eng. Consultant: *Kimley-Horn*
Contract % Complete: *95%*
Eng. Contract Amount: *\$308,970*
Amount Paid to Date: *\$298,085*
Preliminary Plan (30%) Due Date: *Complete*
Final Plan: *Complete*
Bid Set Due Date: *January 2026*
Construction Estimate: *\$5,810,000*

COMMENTS: The design consultant is finalizing the bid set of plans. The project is anticipated to be bid in Spring 2026 to coordinate with the 24" Highway 195 and Chaparral Road Water Line Project.

8. PROJECT NAME: LIFT STATION #1 REHAB

Project Manager: *Steve Kana*
Eng. Consultant: *CP&Y dba STV Infrastructure*
Contract % Complete: *85%*
Eng. Contract Amount: *\$321,375*
Amount Paid to Date: *\$152,321*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *Completed*
Bid Set Due Date: *February 2026*
Construction Estimate: *\$4,695,000*

WATER AND SEWER




COMMENTS: Final design is complete. The construction bid for this project is scheduled for early 2027 once Lift Station #6 rehabilitation is complete. In order to maintain our system Lift Station #6 construction must be complete before construction at Lift Station #1 can begin.

9. PROJECT NAME: SEWER LINE REHABILITATION

Project Manager: *Steve Kana*
Eng. Consultant: *Pipeline Analysis*
Contract % Complete: *99%*
Eng. Contract Amount: *\$628,292*
Amount Paid to Date: *\$591,083*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *Completed*
Bid Set Due Date: *Completed*
Construction Estimate: *\$10,260,453*

WATER AND SEWER

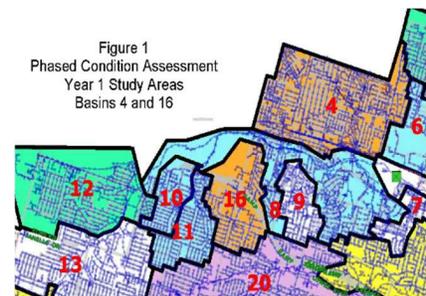

COMMENTS: Phase 1 of the sanitary sewer evaluation survey (SSES) consists of Basins 4 and 16. There are 1,172 manholes and 327,549 feet of sewer main that will be evaluated in Phase 1. All evaluations are complete. Staff is preparing construction documents for the first Phase.

10. PROJECT NAME: REUSE WATER FOR COMMUNITY CENTER WATER AND SEWER


Project Manager: *Steve Kana*
Eng. Consultant: *Garver, LLC*
Contract % Complete: *0%*
Eng. Contract Amount: *\$151,908*
Amount Paid to Date: *\$0.00*
Preliminary Plan (30%) Due Date: *TBD*
Final Plan Due Date: *TBD*
Bid Set Due Date: *TBD*
Construction Estimate: *\$1,300,000*



COMMENTS: This project will provide reuse water to the Community Center irrigation system. Using reuse water for irrigation reduces the need for treated water. An agreement with Garver, LLC, for engineering design and contract administration was approved by the city council on January 6th, 2026. This project will be funded by Community Development Block Grant and Water & Sewer Capital Improvement Plan funds.

11. PROJECT NAME: W.S. YOUNG DRIVE & I-14 INTERSECTION DRAINAGE IMPROVEMENT

Project Manager: *Nilka E Rosado*
Eng. Consultant: *Walker Partners*
Contract % Complete: *78%*
Eng. Contract Amount: *\$68,700*
Amount Paid to Date: *\$ 53,427*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *Completed*
Bid Set Due Date: *February 2026*
Construction Estimate: *TBD*

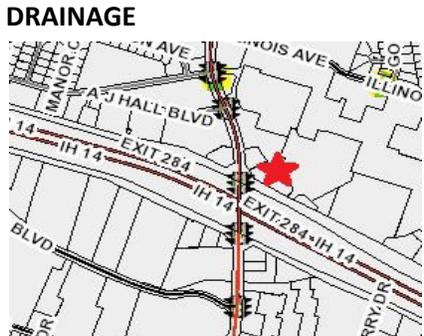


COMMENTS: Final plans have been reviewed and accepted. The bid packet has been prepared, and the project will move to bidding in March 2026.

12. PROJECT NAME: DRAINAGE MASTER PLAN/STUDY

Project Manager: *Nilka E Rosado*
Eng. Consultant: *Scheibe Consulting, LLC*
Contract % Complete: 86%
Eng. Contract Amount: *\$422,810*
Eng. Contract Amendment: *\$62,810*
Amount Paid to Date: *\$365,805*
Preliminary Report Date: *Completed 2025*
Final Plan Due Date: *February 2026*
Bid Set Due Date: *N/A*
Construction Estimate: *N/A*

DRAINAGE

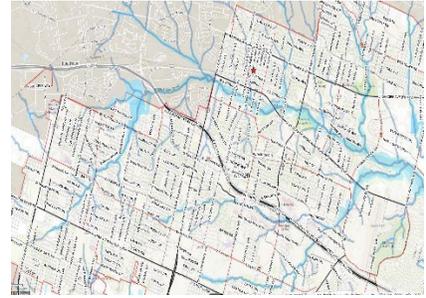

COMMENTS: The Letter of Map Revision (LOMR) has been reviewed by the city and submitted to the Federal Emergency Management Agency (FEMA). As a result of this review, five proposed projects have been included in the Lower Brazos Regional Flood Plan as part of the City's future projects.

13. PROJECT NAME: STONETREE DRIVE DRAINAGE IMPROVEMENTS

Project Manager: *Nilka E Rosado*
Eng. Consultant: *CP&Y dba STV Infrastructure*
Contract % Complete: 51%
Eng. Contract Amount: *\$158,611*
Eng. Contract Amendment: *\$31,301*
Amount Paid to Date: *\$ 81,250*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *February 2026*
Bid Set Due Date: *March 2026*
Construction Estimate: *TBD*

DRAINAGE



COMMENTS: Contract Amendment No. 1 has been submitted and approved by the City for additional survey at the airport. Updated plans will be submitted in February 2026.

14. PROJECT NAME: Saddle Ridge Park Improvements

Project Manager: *Nilka E Rosado*
Eng. Consultant: *Walker Partners*
Contract % Complete: *.07%*
Eng. Contract Amount: *\$49,000*
Amount Paid to Date: *\$ 3,500.00*
Preliminary Plan (30%) Due Date: *Completed*
Final Plan Due Date: *February 2026*
Bid Set Due Date: *March 2026*
Construction Estimate: *TBD*

DRAINAGE



COMMENTS: City staff met with the consultant and clarified comments on the 30% submittal. The consultant is currently working on the final plans updates to submit them in February.

15. PROJECT NAME: FIRE STATION NO. 5

Project Manager: *Yul Eroy*
Eng. Consultant: *Martinez Architects*
Contract % Complete: *0%*
Eng. Contract Amount: *TBD*
Amount Paid to Date: *\$0*
Preliminary Plan (30%) Due Date: *TBD*
Final Plan Due Date: *TBD*
Bid Set Due Date: *TBD*
Construction Estimate: *TBD*

FACILITIES



COMMENTS:

The city has negotiated the land acquisition with KISD, and an agreement will be presented at the January 20, 2026, city council meeting for approval.

16. PROJECT NAME: ROSEWOOD – ASPEN DRIVE TRAFFIC SIGNAL

Project Manager: *Donald Wetzel*
Eng. Consultant: *Kimley-Horn and Associates*
Contract % Complete: *0%*
Eng. Contract Amount: *\$89,330.00*
Amount Paid to Date: *\$0.00*
Preliminary Plan (30%) Due Date: *Pending*
Final Plan Due Date: *Pending*
Bid Set Due Date: *Pending*
Construction Estimate: *\$8,635,985*

TRANSPORTATION



COMMENTS: On December 12, 2025, the City approved a contract for the design of a new traffic signal at the intersection of Rosewood and Aspen Drive(s). A kick-off meeting will be held in the second week of January 2026. We are awaiting the design engineer's project schedule.

17. PROJECT NAME: TRIMMIER ROAD–10TH ST. AT HALLMARK AVE

Scope: *Drainage Improvements*

Project Manager: *TBD*

Eng. Consultant: *TBD*

Engineer's Estimated Cost: *\$TBD*

Re-Bid Opening Date: *TBD*

Apparent Low Bidder: *TBD*

Construction Estimate: *TBD*

DRAINAGE



COMMENTS:

The city is reviewing options for a redesign of this project.

SECTION II PROJECTS IN BID OR CONTRACT PHASE

- PROJECT NAME:** CHAPARRAL ROAD TRAFFIC SIGNALS
Scope: *Install Traffic Signals for Safety Improvements*
Project Manager: *Donald Wetzel*
Eng. Consultant: *Freese and Nichols, Inc.*
Engineer's Estimated Cost: *\$593,850.00*
Bid Opening Date: *TBD*
Apparent Low Bidder: *TBD*
Construction Estimate: *TBD*

TRANSPORTATION



COMMENTS:

The city is working with Bell County to secure approval of an Interlocal Agreement to fund the traffic signals. Once funding is approved, the City will proceed with bidding for this project.

- PROJECT NAME:** CHAPARRAL ROAD TRAFFIC SIGNALS
Scope: *Install Traffic Signals for Safety Improvements*
Project Manager: *Donald Wetzel*
Eng. Consultant: *Freese and Nichols, Inc.*
Engineer's Estimated Cost: *\$593,850.00*
Bid Opening Date: *TBD*
Apparent Low Bidder: *TBD*
Construction Estimate: *TBD*

TRANSPORTATION



COMMENTS:

The city is working with Bell County to secure approval of an Interlocal Agreement to fund the traffic signals. Once funding is approved, the City will proceed with the bidding the project.

SECTION III PROJECTS UNDER CONSTRUCTION

- PROJECT NAME:** BUNNY TRAIL RECONSTRUCTION
Scope: Road Replacement and Drainage Improvements
Project Manager: *Christopher Hoch*
Contractor: *RT Schneider Const. Co., Ltd.*
Contact: *Bryant Davis*
Construction Contract Amount: *\$5,814,103*
Construction Start Date: *July 2024*
Percent Complete: *87%*
Est. Completion Date: *December 2025*
Amount Paid to Date: *\$5,095,065.10*

TRANSPORTATION



COMMENTS: Construction is substantially complete, with only punch-list items remaining. A ribbon-cutting ceremony is anticipated in the first quarter of 2026.

- PROJECT NAME:** GILMER STREET RECONSTRUCTION
Scope: Rebuilding Roadway and Sidewalks
Project Manager: *Donald Wetzel*
Contractor: *TTG Utilities, Inc.*
Contact: *Keith James*
Construction Contract Amount: *\$4,957,916*
Construction Start Date: *January 2024*
Percent Complete: *72%*
Est. Completion Date: *2nd Quarter 2026*
Amount Paid to Date: *\$3,392,256*

TRANSPORTATION



COMMENTS: The contractor has completed curb and gutter, sidewalks, and driveways. The contractor will begin paving the roadway in January between Tank Battalion and Rancier Avenue. The roadway will be open to two-way traffic in February 2026. The last major item is Phase 5 included the railroad crossing, which is being done by BNSF, and is due to start at the end of January 2026

- 3. **PROJECT:** WATERCREST RECONSTRUCTION
Scope: Rebuilding Roadway and Sidewalks
 Project Manager: *Donald Wetzel & Chris Hoch*
 Contractor: *Cash Construction, Inc.*
 Contact: *Cristina Martinka*
 Construction Contract Amount: \$12,462,678
 Construction Start Date: *October 2024*
 Percent Complete 22%
 Est. Completion Date: *August 2026*
 Amount Paid to Date: \$2,770,298.79

TRANSPORTATION



COMMENTS: The contractor is installing the concrete curb and gutter and a six-foot sidewalk and removing and replacing unacceptable base material. The original base material did not meet the city’s specifications. Asphalt paving is anticipated to begin in February on the south side of the roadway.

- 4. **PROJECT NAME:** STAGECOACH RECONSTRUCTION PHASE 1
Scope: Full-depth reconstruction of Stagecoach Road
 Project Manager: *Christopher Hoch*
 Contractor: *JHL Construction*
 Contact: *Donna Walter*
 Construction Contract Amount: \$7,716,902
 Construction Start Date: *July 2025*
 Percent Complete: 14%
 Est. Completion Date: *Summer 2026*
 Amount Paid to Date: \$1,139,119.69.

TRANSPORTATION



COMMENTS: The contractor has completed removal of the unacceptable base material and has been installing the new base material along the full length of the roadway. Asphalt paving on the northern side is anticipated to begin in February 2026.

- 5. **PROJECT NAME:** CHAPARRAL PUMP STATION
Scope: New 8 MGD PS for Upper Pressure Plane
 Project Manager: *Steve Kana*
 Contractor: *SSP Industries*
 Contact: *Ron Fournier*
 Construction Contract Amount: \$8,045,908
 Construction Start Date: *March 2024*
 % Complete: 94%
 Estimated Completion Date: *March 2026*
 Amount Paid to Date: \$7,398,822

WATER AND SEWER



COMMENTS: The contractor has completed all building items for this project project, including the building, electrical, piping, pumps, and generator. The contractor is currently working on the site and laying asphalt. The project has an initial startup scheduled for February 2026.

6. PROJECT NAME: PUMP STATION #2 UPGRADES

Scope: Pump Station Upgrades

Project Manager: *Steve Kana*

Contractor: *Barsh Construction*

Contact: *Tommy Fulford*

Construction Contract Amount: *\$2,272,859*

Construction Start Date: *May 2024*

% Complete: *97%*

Estimated Completion Date: *January 2026*

Amount Paid to Date: *\$2,152,537*

WATER AND SEWER



COMMENTS: This project is considered substantially complete, with only punch-list items remaining.

7. PROJECT NAME: WATER LINE REHAB PHASE 1

Scope: Replacement of 18 failed water lines

Project Manager: *Steve Kana*

Contractor: *Insituform Technologies*

Contact: *Tim Naylor*

Construction Contract Amt: *\$2,798,170*

Construction Start Date: *January 2025*

% Complete: *93%*

Estimated Completion Date: *January 2026*

Amount Paid to Date: *\$1,721,161*

WATER AND SEWER



COMMENTS: The contractor has completed 16 of the 18 water line replacements. Due to difficulties with their boring equipment and other factors, the contractor is behind schedule. Due to these issues, the assessment of Liquidated Damages began on September 18, 2025. Replacement of a water line along Dimple Street, which includes a creek crossing and the replacement of a 2" water line along Fort Hood Street north of Veterans Memorial Boulevard, remains.

8. PROJECT NAME: WATER METER REPLACEMENT PHASE 3

Scope: Installation of 5,000 Meters and Radios

Project Manager: *Steve Kana*

Contractor: *Aqua-Metric*

Contact: *Scott Kohan*

Construction Contract Amount: *\$1,974,045*

Construction Start Date: *January 2026*

Percent Complete: *0%*

Estimated Completion Date: *September 2026*

Amount Paid to Date: *\$0.00*

WATER AND SEWER



COMMENTS: 4,544 residential and 288 larger commercial meters have been ordered. The contract to purchase the radios and install all the meters, radios, and AMI software was approved by the City Council on October 21, 2025. This project will be completed by September 2026.

9. PROJECT NAME: RE-USE WATER FOR GOLF COURSE
Scope: 100,000 gal. steel GST tank for golf course irrigation
 Project Manager: *Steve Kana*
 Contractor: *Bell Contractors*
 Contact: *Jonathan Perez*
 Construction Contract Amount: *\$770,369*
 Construction Start Date: *September 2025*
 Percent Complete: *75%*
 Est. Completion Date: *February 2026*
 Amount Paid to Date: *\$480,224*


WATER AND SEWER



COMMENTS: The contractor has built the tank and installed all site piping. The painting of the tank, electrical work, and SCADA installation will begin in January.

10. PROJECT NAME: KILLEEN COMMUNITY CENTER
Scope: Rehabilitation of Existing Building
 Project Manager: *Yul Eroy*
 Construction Inspection Consultant: *MRB Group*
 Construction Inspection Amount: *\$170,100*
 Construction Contractor: *HCS, Inc.*
 Construction Contract Amount: *\$9,133,571*
 Percent Complete: *72%*
 Estimated Completion Date: *May 2026*
 Amount Paid to Date: *\$6,576,900.85*


FACILITIES

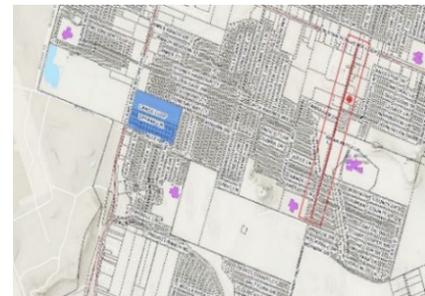

COMMENTS: HCS, Inc continues construction activities, including concrete work at 95% done, structural steel installation 100% completed, electrical work at 80%, storefront doors and windows at 90% completed, and construction of the pickleball court at 80% done. The contractor is working to complete the installation of the new roof on the building. The contractor estimates the roof will be completed by the end of January. The focus will then shift to the interior work.

11. PROJECT NAME: SIDEWALK & ADA RAMP IMPROVEMENTS
Scope: Improvement of ADA ramps and sidewalks in 10 locations across the city.
 Project Manager: *Yul Eroy*
 Contractor: *Jerdon Enterprise, LP*
 Construction Contract Amount: *\$613,155*
 Construction Start Date: *October 2024*
 Percent Complete: *100%*
 Est. Completion Date: *November 2025*
 Amount Paid to Date: *\$613,155*

RECREATION/TRANSPORTATION

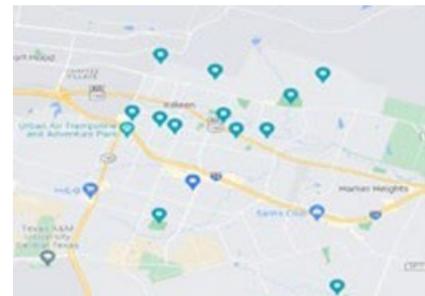

COMMENTS: The project construction is complete. The city is now in the process of closing out the project.

12. PROJECT NAME: TRANSFER WASTE STATION TUNNEL MODIFICATIONS

Scope: Facility Upgrade Construction
Project Manager: *Donald Wetzel*
Contractor: *Jamail & Smith Construction*
Contact: *Kyle Franz*
Construction Contract Amount: *\$960,929*
Construction Start Date: *February 2025*
Percent Complete: *93%*
Est. Completion Date: *February 2026*
Amount Paid to Date: *\$900,217*

FACILITIES



COMMENTS: The contractor is in the final phase of the construction for this project. The project is expected to be completed in February 2026.

13. PROJECT NAME: TRANSFER WASTE STATION PUSHWALL

Scope: Repair Facilities Pushwall
Project Manager: *Donald Wetzel*
Contractor: *Jamail & Smith Construction*
Contact: *Kyle Franz*
Construction Contract Amount: *\$202,703*
Construction Start Date: *March 2025*
Percent Complete: *98%*
Est. Completion Date: *December 2025*
Amount Paid to Date: *\$199,452*

FACILITIES



COMMENTS: The project construction is completed. The city is now in the process of closing out the project.

14. PROJECT NAME: 24" HWY 195 & CHAPARRAL WATER LINE

Scope: Construction of a 24" water line
Project Manager: *Steve Kana*
Contractor: *Blackrock Construction*
Contact: *Carlos Jimenez*
Construction Contract Amount: *\$9,981,018*
Construction Start Date: *December 2025*
Percent Complete: *5%*
Est. Completion Date: *May 2027*
Amount Paid to Date: *\$0.00*

WATER AND SEWER



COMMENTS: Blackstone Construction began construction on December 15, 2025. They are installing the water line along Hwy. 195 and will begin installing the water line along Chaparral the week of January 19th.

15. PROJECT NAME: LIFT STATION #6 REHAB & EXPANSION

Scope: Rehabilitation & 7 MGD expansion of existing LS

Project Manager: *Steve Kana*

Contractor: *Bell Contractors*

Contact: *Jonathan Perez*

Construction Contract Amount: *\$6,961,950*


Construction Start Date: *December 2025*

Percent Complete: *0%*

Est. Completion Date: *April 2027*

Amount Paid to Date: *\$0.00*

WATER AND SEWER

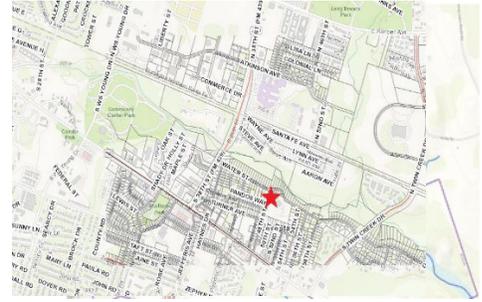

COMMENTS: The Notice to Proceed was issued to Bell Contractors with a contract start date of December 1, 2025. The contractor has been submitting their material and equipment submittals and preparing to start construction on January 19, 2025.

16. PROJECT NAME: FLEET SERVICES FACILITY

Scope: *Construction of a new Fleet Services Facility*

Project Manager: *Christopher Hoch*

Contractor: *CORE Construction*

Contact: *Jennifer Martin*

Construction Contract Amount: *\$16,689,753*

Construction Start Date: *August 2026*

Percent Complete: *0%*

Est. Completion Date: *TBD*

Amount Paid to Date: *\$0.00*

FACILITIES



COMMENTS: The contractor has completed the site survey and met with the appropriate city department. Work on the layout of the new facility has begun. This project is part of an overall design-build package. CORE Construction is responsible for both the design and construction of this project. Construction is anticipated to start in the Fall of 2026.

SECTION IV PRIVATE DEVELOPMENT

Single Family / Multi-Family Residential

- 1. PROJECT NAME:** *HERITAGE OAKS PHASE SEVEN*
Location: *Rosewood Drive & Chaparral Road*
Developer/Contractor: *Killeen Chaparral Development, LLC/Purser Construction*
Contact: *Gary W. (Bubba) Purser, Jr*
Project Current Phase: *Closeout*
City Inspector: *R. Havens* Plans Released: *03/21/2024*
% Complete Construction: *100%* Completion Date: *09/30/2024*

COMMENTS:

Letter of Lot Release Issued 09/10/2024

Maintenance Bonds Issued:

2 Year - Water exp. 09/2026

2 Year - Streets exp. 09/2026

2 Year - Sewer exp. 09/2026

2 Year - Drainage exp. 09/2026

- 2. PROJECT NAME:** *SC22-10 MITCHELL FARM PHASE II*
Location: *7630 Clear Creek Road*
Developer/Contractor: *J Squared Killeen Development, LLC/Purser Construction*
Contact: *Josh Welch*
Project Current Phase: *Closeout*
City Inspector: *L. Eteuati* Plans Released: *11/9/2022*
% Complete Construction: *100%* Completion Date: *01/31/2025*

COMMENTS:

Letter of Lot Release Issued 02/10/2025

Maintenance Bonds Issued:

2 Year - Water exp. 01/2027

2 Year - Streets exp. 01/2027

2 Year - Sewer exp. 01/2027

2 Year - Drainage exp. 01/2027

- 3. PROJECT NAME:** *SC22-12 REYNOLDS CROSSING PHASE I*
 Location: *E. Rancier Avenue at Prairie Clover Road*
 Developer/Contractor: *Northridge Land Investments, LLC/Bell Contractors, and S3 Site Work*
 Contact: *Josh Welch*
 Project Current Phase: *Closeout*
 City Inspector: *K. McBride* Plans Released: *11/15/2022*
 % Complete Construction: *100%* Completion Date: *03/2/2024*

COMMENTS:

Letter of Lot Release Issued 03/21/2024

Maintenance Bonds Issued:

2 Year - Water exp. 03/2026

2 Year - Streets exp. 03/2026

2 Year - Sewer exp. 03/2026

2 Year - Drainage exp. 03/2026

- 4. PROJECT NAME:** *SC22-14 RAHMAN SUBDIVISION PHASE IV*
 Location: *500 Omar Drive*
 Developer/Contractor: *Dr. Muhammad Khan*
 Contact: *Lina Chatay*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez* Plans Released: *09/12/2024*
 % Complete: *90%* Est. Completion Date: *03/2026*

- 5. PROJECT NAME:** *SC22-15 VICTORY RANCH PHASE I*
 Location: *5901 S. Fort Hood Street*
 Developer/Contractor: *Cactus Jack Development, Inc.*
 Contact: *Joey Theriot*
 Project Current Phase: *Closeout*
 City Inspector: *L. Eteuati* Plans Released: *02/22/2023*
 % Complete: *100%* Completion Date: *03/31/2024*

COMMENTS:

Letter of Lot Release Issued 4/2/2024

Maintenance Bonds Issued:

2 Year - Water exp. 03/2026

2 Year - Streets exp. 03/2026

2 Year - Sewer exp. 03/2026

2 Year - Drainage exp. 03/2026

6. PROJECT NAME: *SC22-15 THE ROOST ADDITION PHASE 2*
 Location: *4302 Cunningham Road*
 Developer/Contractor: *Rachiii Brothers, LLC – Series 101/Riley Scott Construction*
 Contact: *Pedro Quintero*
 Project Current Phase: *Closeout*
 City Inspector: *R. Havens* Plans Released: *06/8/2023*
 % Complete: *100%* Completion Date: *11/30/2024*

COMMENTS:
 Letter of Lot Release Issued *12/10/2024*

Maintenance Bonds Issued:
 2 Year - Water exp. *12/2026* 2 Year - Streets exp. *12/2026*
 2 Year - Sewer exp. *12/2026* 2 Year - Drainage exp. *12/2026*

7. PROJECT NAME: *SC22-18 HERRING LEGACY ESTATES PHASE 2*
 Location: *740 Money Pit Road*
 Developer/Contractor: *Herring Legacy Developers, Inc.*
 Contact: *Ace Reneau*
 Project Current Phase: *Closeout*
 City Inspector: *R. Havens* Plans Released: *09/15/2023*
 % Complete: *100%* Est. Completion Date: *03/15/2025*

COMMENTS:
 Letter of Lot Release Issued *03/20/2025*

Maintenance Bonds Issued:
 2 Year - Water exp. *02/2027* 2 Year - Streets exp. *02/2027*
 2 Year - Sewer exp. *02/2027* 2 Year - Drainage exp. *02/2027*

8. PROJECT NAME: *SC23-01 MORRIS SUBDIVISION PHASE 6*
 Location: *1010 Anna Lee Drive*
 Developer/Contractor: *Killeen Summit Builders, LLC.*
 Contact: *Ace Reneau*
 Project Current Phase: *Closeout City*
 Inspector: *L. Eteuati* Plans Released: *03/14/2024*
 % Complete Construction: *100%* Est. Completion Date: *12/2025*

COMMENTS: Plans for construction were released as of *3/14/2024*.

9. PROJECT NAME: *SC23-02 THE PRESERVE AT THOUSAND OAKS PHASE I*
Location: *4244 Stagecoach Road*
Developer/Contractor: *Flintrock Builders*
Contact: *Joseph Theriot*
Project Current Phase: *Under Construction*
City Inspector: *V. Lopez* Plans Released: *11/6/2024*
% Complete: *100%* Est. Completion Date: *03/2025*

COMMENTS:
Letter of Lot Release Issued *03/03/2025*

Maintenance Bonds Issued:
2 Year - Water exp. *03/2027* 2 Year - Streets exp. *03/2027*
2 Year - Sewer exp. *03/2027* 2 Year - Drainage exp. *03/2027*

10. PROJECT NAME: *DOGWOOD ADDITION*
Location: *Dogwood Blvd. at East Veterans Memorial Blvd.*
Developer/Contractor: *Flintrock Builders*
Contact: *Joseph Theriot*
Project Current Phase: *Closeout*
City Inspector: *K. McBride* Plans Released: *07/5/2024*
% Complete Construction: *100%* Est. Completion Date: *03/20/2025*

COMMENTS:
Letter of Lot Release Issued *03/20/2025*

Maintenance Bonds Issued:
2 Year - Water exp. *01/2027* 2 Year - Streets exp. *01/2027*
2 Year - Sewer exp. *01/2027* 2 Year - Drainage exp. *01/2027*

11. PROJECT NAME: *SC22-02 TURNBO RANCH PHASE V*
Location: *Chaparral Road at Trimmier Road*
Developer/Contractor: *WBW Development Group, LLC – Series 016*
Contact: *Dillon Whitis*
Project Current Phase: *Closeout*
City Inspector: *R. Havens* Plans Released: *08/07/2024*
% Complete Construction: *100%* Est. Completion Date: *06/30/2025*

COMMENTS: *Water and Wastewater Only*
Maintenance Bonds Issued:
2 Year - Water exp. *06/2026*
2 Year - Sewer exp. *06/2026*

COMMENTS: *Water and Wastewater only.*

- 12. PROJECT NAME:** *SC24-05 LIONS GATE ESTATE*
 Location: *409 Reese Creek Road*
 Developer/Contractor: *Michael Agyemang-Amoako*
 Contact: *Paul Jordan*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati* Plans Released: *07/25/2024*
 % Complete Construction: *95%* Est. Completion Date: *11/15/2025*
- 13. PROJECT NAME:** *SC24-06 REYNOLDS CROSSING PHASE II*
 Location: *E. Rancier Avenue at Prairie Clover Road*
 Developer/Contractor: *Northridge Land Investments, LLC/Bell Contractors, and S3 Site Work*
 Contact: *Josh Welch*
 Project Current Phase: *Closeout*
 City Inspector: *K. McBride* Plans Released: *11/19/2024*
 % Complete Construction: *90%* Est. Completion Date: *02/01/2026*
- 14. PROJECT NAME:** *SC24-07 THE PRESERVE AT A THOUSAND OAKS PHASE II AND III*
 Location: *4244 Stagecoach Road*
 Developer/Contractor: *Flintrock Builders*
 Contact: *Craig Langford II*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez* Plans Released: *02/26/2025*
 % Complete Construction: *75%* Est. Completion Date: *04/28/2026*
- 15. PROJECT NAME:** *TURNBO RANCH PHASE IV*
 Location: *Chaparral Road at Trimmier Road*
 Developer/Contractor: *WBW Development Group, LLC – Series 045*
 Contact: *Dillon Whitis*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez* Plans Released: *12/04/2024*
 % Complete Construction: *30%* Completion Date: *03/30/2026*
- 16. PROJECT NAME:** *VICTORY RANCH PHASE II*
 Location: *5901 S. Fort Hood Street*
 Developer/Contractor: *Cactus Jack Developments, Inc.*
 Contact: *Joey Theriot*
 Project Current Phase: *Closeout*
 City Inspector: *L. Eteuati* Plans Released: *01/08/2025*
 % Complete Construction: *100%* Completion Date: *12/31/2025*

COMMENTS:

Letter of Lot Release Issued 08/20/2025

Maintenance Bonds Issued:

2 Year - Water exp. 07/2027

2 Year - Sewer exp. 07/2027

2 Year - Streets exp. 07/2027

2 Year - Drainage exp. 07/2027

- 17. PROJECT NAME:** *TURNBO RANCH PHASE VI*
 Location: *Chaparral Road at Trimmier Road*
 Developer/Contractor: *WBW Development Group, LLC – Series 045*
 Contact: *Dillon Whitis*
 Project Current Phase: *Under Construction*
 City Inspector: *R. Havens* Plans Released: *03/05/2025*
 % Complete Construction: *30%* Completion Date: *03/30/2026*
- 18. PROJECT NAME:** *VICTORY RANCH PHASE IV*
 Location: *5901 S. Fort Hood Street*
 Developer/Contractor: *Cactus Jack Developments, Inc.*
 Contact: *Joey Theriot*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati* Plans Released: *05/02/2025*
 % Complete Construction: *10%* Completion Date: *10/31/2026*
- 19. PROJECT NAME:** *TURNBO RANCH PHASE VIII*
 Location: *Chaparral Road at Trimmier Road*
 Developer/Contractor: *WBW Development Group, LLC – Series 052*
 Contact: *Dillon Whitis*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez* Plans Released: *8/14/2025*
 % Complete Construction: *5%* Completion Date: *03/30/2026*
- 20. PROJECT NAME:** *Southwest Crossing Fourth Replat*
 Location: *Trimmier Road at Turkey Trot Road*
 Developer/Contractor: *Central Texas Land Development Services, LLC*
 Contact: *Garrett Marburger*
 Project Current Phase: *In Design*
 City Inspector: *V. Lopez* Plans Released: *N/A*
 % Complete Construction: *0%* Completion Date: *N/A*
- 21. PROJECT NAME:** *Cosper Creek Replat No. 3 Phases 1-3*
 Location: *Trimmier Road at Chaparral Road*
 Developer/Contractor: *Arrowhead Developers, LLC*
 Contact: *Jerome Gomer*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez* Plans Released: *10/9/2025*
 % Complete Construction: *0%* Completion Date: *10/31/2026*

- 22. PROJECT NAME:** *Bunny Trails – Phase I*
Location: *6603 Bunny Trail*
Developer/Contractor: *Bunny Trail Real Estate, LP*
Contact: *Uday Vadapalli*
Project Current Phase: *In Design*
City Inspector: *L. Eteuati* Plans Released: *N/A*
% Complete Construction: *0%* Completion Date: *N/A*
- 23. PROJECT NAME:** *Herring Legacy Phase 3*
Location: *East Trimmier Road at Chaparral Road*
Developer/Contractor: *Central Texas Land Development Services, LLC*
Contact: *B. Clement*
Project Current Phase: *In Design*
City Inspector: *V. Lopez* Plans Released: *N/A*
% Complete Construction: *0%* Completion Date: *N/A*

Commercial

- 24. PROJECT NAME:** *West View Retail*
Location: *2104 Clear Creek Road*
Project Current Phase: *Under Construction*
City Inspector: *L. Eteuati*
% Complete Construction: *95%*
Plans Released: *07/26/2023*
Permit No: *Pre-MGO*
- 25. PROJECT NAME:** *Goodwill Stores*
Location: *4901 W. Stan Schlueter Loop*
Project Current Phase: *Under Construction*
City Inspector: *L. Eteuati*
% Complete Construction: *95%*
Plans Released: *03/28/2024*
Permit No: *2023-1157*
- 26. PROJECT NAME:** *J NV Central Texas*
Location: *807 N. Twin Creek Drive*
Project Current Phase: *Under Construction*
City Inspector: *K. McBride*
% Complete Construction: *95%*
Plans Released: *01/11/2024*
Permit No: *2024-266*
- 27. PROJECT NAME:** *Rosewood C-Store*
Location: *2201 Rosewood Drive*
Project Current Phase: *Under Construction*
City Inspector: *V. Lopez*
% Complete Construction: *65%*
Plans Released: *01/2/2024*
Permit No: *2024-247*
- 28. PROJECT NAME:** *Mighty Wash*
Location: *3805 E. Stan Schlueter Loop*
Project Current Phase: *Under Construction*
City Inspector: *V. Lopez*
% Complete Construction: *85%*
Plans Released: *06/06/2024*
Permit No: *2024-495*
- 29. PROJECT NAME:** *MetroNet Communications*
Location: *500 Stefek Drive*
Project Current Phase: *Under Construction*
City Inspector: *V. Lopez*
% Complete Construction: *90%*
Plans Released: *06/18/2024*
Permit No: *2024-1039*
- 30. PROJECT NAME:** *Oncor Substation*
Location: *2900 Elms Drive*
Project Current Phase: *Under Construction*
City Inspector: *L. Eteuati*
% Complete Construction: *95%*
Plans Released: *08/20/2024*
Permit No: *2024-1233*
- 31. PROJECT NAME:** *Avanti Legacy Parkview*
Location: *51 N. W.S. Young Drive*
Project Current Phase: *Under Construction*
City Inspector: *K. McBride*
% Complete Construction: *95%*
Plans Released: *08/20/2024*
Permit No: *2023-1383*
- 32. PROJECT NAME:** *C-Store and Driveway*
Location: *7908 Clear Creek Road*
Project Current Phase: *Under Construction*
City Inspector: *L. Eteuati*
% Complete Construction: *80%*
Plans Released: *06/18/2024*
Permit No: *2024-3012*
- 33. PROJECT NAME:** *R&K Business Plaza*
Location: *5101 Trimmier Road*
Project Current Phase: *Under Construction*
City Inspector: *V. Lopez*
% Complete Construction: *75%*
Plans Released: *9/26/2024*
Permit No: *2024-901*

- 34. PROJECT NAME:** *Platinum RV & Storage*
 Location: *10201 Trimmer Road*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *35%*
 Plans Released: *12/11/2024*
 Permit No: *2024-1376*
- 35. PROJECT NAME:** *G3 Church*
 Location: *1925 E. Elms Road*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *90%*
 Plans Released: *12/02/2024*
 Permit No: *2024-7074*
- 36. PROJECT NAME:** *Killeen Workspace USA*
 Location: *905 Progress Drive*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *80%*
 Plans Released: *12/16/2024*
 Permit No: *2024-7200*
- 37. PROJECT NAME:** *Bates Nissan*
 Location: *5401 Martin Luther King Jr. Blvd.*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *40%*
 Plans Released: *11/21/2024*
 Permit No: *2024-7657*
- 38. PROJECT NAME:** *Amy's Attic*
 Location: *3216 Stagecoach Road*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *90%*
 Plans Released: *12/20/2024*
 Permit No: *2024-8503*
- 39. PROJECT NAME:** *O'Reilly Auto Parts*
 Location: *1700 S. Fort Hood Street*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *95%*
 Plans Released: *12/20/2024*
 Permit No: *2024-585*
- 40. PROJECT NAME:** *Vivian Spa and Nail Bar*
 Location: *1417 W. Stan Schlueter Loop*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *80%*
 Plans Released: *3/14/2025*
 Permit No: *2024-7469*
- 41. PROJECT NAME:** *Delicias Meat Market*
 Location: *2402 W. Stan Schlueter Loop*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *30%*
 Plans Released: *1/31/2025*
 Permit No: *2024-7788*
- 42. PROJECT NAME:** *Long John Silvers*
 Location: *1404 S. Fort Hood Street*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *60%*
 Plans Released: *2/28/2025*
 Permit No: *2024-8301*
- 43. PROJECT NAME:** *Fort Hood Retail*
 Location: *2900 S. Fort Hood Street*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *25%*
 Plans Released: *2/28/2025*
 Permit No: *2024-8887*
- 44. PROJECT NAME:** *First Baptist Church of Killeen*
 Location: *3310 S. W.S. Young Drive*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *50%*
 Plans Released: *2/18/2025*
 Permit No: *2024-11234*
- 45. PROJECT NAME:** *Oncor Substation*
 Location: *1701 Florence Road*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *50%*
 Plans Released: *3/5/2025*
 Permit No: *2025-31*

- 46. PROJECT NAME:** *Dennis Eakin Parking*
 Location: *2301 Rosewood Drive*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *90%*
 Plans Released: *3/26/2025*
 Permit No: *2024-10031*
- 47. PROJECT NAME:** *Bell County Annex*
 Location: *507 N. Gray Street*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *30%*
 Plans Released: *5/7/2025*
 Permit No: *2024-10091*
- 48. PROJECT NAME:** *Featherline Plaza*
 Location: *7950 Featherline Road*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *55%*
 Plans Released: *4/23/2025*
 Permit No: *2024-10575*
- 49. PROJECT NAME:** *Royal Caribbean*
 Location: *1205 Stagecoach Road*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *15%*
 Plans Released: *5/19/2025*
 Permit No: *2025-1829*
- 50. PROJECT NAME:** *Avanti Legacy Westwood*
 Location: *3001 Illinois Ave*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *15%*
 Plans Released: *8/8/2025*
 Permit No: *2025-2586*
- 51. PROJECT NAME:** *Crawford-Bowers*
 Location: *1615 S. Fort Hood St.*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *10%*
 Plans Released: *5/8/2025*
 Permit No: *2025-2725*
- 52. PROJECT NAME:** *KPD Cameras*
 Location: *City Wide*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *90%*
 Plans Released: *9/9/2025*
 Permit No: *2025-4234*
- 53. PROJECT NAME:** *Camelback RV and Storage*
 Location: *1214 Dogwood Blvd.*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *15%*
 Plans Released: *7/30/2025*
 Permit No: *2025-510*
- 54. PROJECT NAME:** *Quik Trip #4177*
 Location: *5551 E. Central Texas Expy*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *70%*
 Plans Released: *5/19/2025*
 Permit No: *2025-1769*
- 55. PROJECT NAME:** *Robinette Gas Station*
 Location: *3900 Robinette Road*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *5%*
 Plans Released: *6/23/2025*
 Permit No: *2025-1771*
- 56. PROJECT NAME:** *5100 Janelle Mixed Use*
 Location: *5100 Janelle Road*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *50%*
 Plans Released: *5/20/2025*
 Permit No: *2025-2075*
- 57. PROJECT NAME:** *4700 S. Fort Hood St. Pad Sites*
 Location: *4700 S. Fort Hood St.*
 Project Current Phase: *Under Construction*
 City Inspector: *V. Lopez*
 % Complete Construction: *90%*
 Plans Released: *7/3/2025*
 Permit No: *2025-6533*

- 58. PROJECT NAME:** *Whitley Steel Retail*
 Location: *3001 S. Fort Hood St.*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *10%*
 Plans Released: *8/18/2025.*
 Permit No: *2025-1389*
- 59. PROJECT NAME:** *Whitley Steel Storage*
 Location: *3025 S. Fort Hood St.*
 Project Current Phase: *Under Construction*
 City Inspector: *L. Eteuati*
 % Complete Construction: *10%*
 Plans Released: *8/18/2025*
 Permit No: *2025-1438*
- 60. PROJECT NAME:** *Murphy Gas Station*
 Location: *500 W. Stan Schluter Loop*
 Project Current Phase: *Under Construction*
 City Inspector: *R. Havens*
 % Complete Construction: *40%*
 Plans Released: *5/19/2025*
 Permit No: *2025-2571*
- 61. PROJECT NAME:** *Avenue Heights Apartments*
 Location: *3000 Illinois Avenue*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *95%*
 Plans Released: *6/18/2024*
 Permit No: *2024-2011*
- 62. PROJECT NAME:** *Dollar General*
 Location: *6612 Clear Creek Road*
 Project Current Phase: *Under Construction*
 City Inspector: *A Eteuati*
 % Complete Construction: *10%*
 Plans Released: *12/4/2025*
 Permit No: *2025-8296*
- 63. PROJECT NAME:** *Dennis Eakin – KIA Addition*
 Location: *5200 E. Central Texas Expy*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *15%*
 Plans Released: *11/29/2025*
 Permit No: *2025-9190*
- 64. PROJECT NAME:** *Liberty Christian Center*
 Location: *54107 Westcliff Road*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction:
 Plans Released: *10/16/25*
 Permit No: *2025-9504*
- 65. PROJECT NAME:** *Killeen Dental Health Center*
 Location: *1405 E. Elms Road*
 Project Current Phase: *Under Construction*
 City Inspector: *K. McBride*
 % Complete Construction: *90%*
 Plans Released: *10/20/2025*
 Permit No: *2025-9658*

DESCRIPTION	PERIOD	TOTALS
PLATS REVIEWED (ALL TYPES)	(10/01/2025 – 12/31/2025)	20
ZONING CASES	(10/01/2025 – 12/31/2025)	17
64FLUM CASES	(10/01/2025 – 12/31/2025)	2
5COMMERCIAL PLAN REVIEWS	(10/01/2025 – 12/31/2025)	10
RIGHT-OF-WAY PERMITS	(10/01/2025 – 12/31/2025)	139

SECTION VI GEOGRAPHIC INFORMATION SYSTEMS (GIS)

1. **PROJECT NAME:** Arbor Day web map update
Location: GIS Portal
Status: Completed
Completion Date: November 2025
2. **PROJECT NAME:** Parks Data Collection
Location: Various Parks
Status: *In Progress, Ongoing – 65% completed*
Completion Date: *To be determined*
3. **PROJECT NAME:** Neighborhood map
City Residential Development broken down by Neighborhoods.
Status: *In progress, On Hold, staff comments pending*
Completion Date: *To be determined*
4. **PROJECT NAME:** ADA Data updates to GIS
GIS Data received from the contractor; the data is currently under review.
Location: *N/A*
Status: *Ongoing*
Completion Date: *To be determined*
5. **PROJECT NAME:** Geo-Locate Permit Application
A GIS web mapping application for displaying permit information.
Location: *GIS Portal*
Status: *In Discovery Phase*
Completion Date: *To be determined*
6. **PROJECT NAME:** City Signs data update to GIS
Updates to the city-maintained signs GIS feature
Location: *Citywide*
Status: *In progress, Ongoing*
Completion Date: *To be determined*
